

Item 11: Community

11.1 Mudgee Arts Precinct Construction - Project Update

REPORT BY THE DIRECTOR COMMUNITY
TO 17 AUGUST 2022 ORDINARY MEETING
GOV400098, COR400301, REC800038

RECOMMENDATION

That Council note the report by the Director Community on the Mudgee Arts Precinct Construction - Project Update.

Executive summary

The attached report provides an update on the Progress of the Mudgee Arts Precinct Project.

Disclosure of Interest

Nil

Detailed report

The Mudgee Arts Precinct Project is a major project that has attracted \$5.3 million in State and Federal funding from a total budget of \$8.1 million.

The project continues to progress with several successful exhibitions having taken place.

Construction on the workshop building has commenced and is running to schedule with fit out of furniture to be installed in August and project completion expected by the end of September.

Community Plan implications

Theme	Looking After Our Community
Goal	Meet the diverse needs of the community and create a sense of belonging
Strategy	Support arts and cultural development across the Region

Strategic implications

Council Strategies

Community Strategic Plan

Council Policies

Not Applicable

Legislation

Not Applicable

Financial implications

Not Applicable

Associated Risks

Regular reporting to Council provides an opportunity to communicate and manage any ongoing unexpected risks that emerge with this project.

SIMON JONES
DIRECTOR COMMUNITY

26 July 2022

Attachments: 1. Mudgee Arts Precinct Progress Update.

APPROVED FOR SUBMISSION:

BRAD CAM
GENERAL MANAGER



MUDGEE ARTS
PRECINCT PROJECT
PROGRESS REPORT

25 JULY 2022

MID-WESTERN REGIONAL COUNCIL
COMMUNITY

■ ■ ■ ■ ■ TOWARDS 2030



COMMUNITY | MUDGEES ARTS PRECINCT PROJECT PROGRESS REPORT

Project Update

As at 25 July 2022 the overall project progress for the Mudgee Arts Precinct Project was approximately 90%.

OVERALL PROJECT PROGRESS




GALLERY AND TOURISM BUILDING PROGRESS



WORKSHOP BUILDING PROGRESS



PROJECT EXPENDITURE



COMMUNITY


Achievements and Highlights

- Construction commenced on workshop building
- Painting and gyprock complete
- Flooring, kitchen and wash up cabinetry has been installed
- Electrical works and concreting has commenced

The Next 6 Months

- New fencing and landscaping
- New parking areas constructed
- Fit-out of workshop spaces

PHOTOS

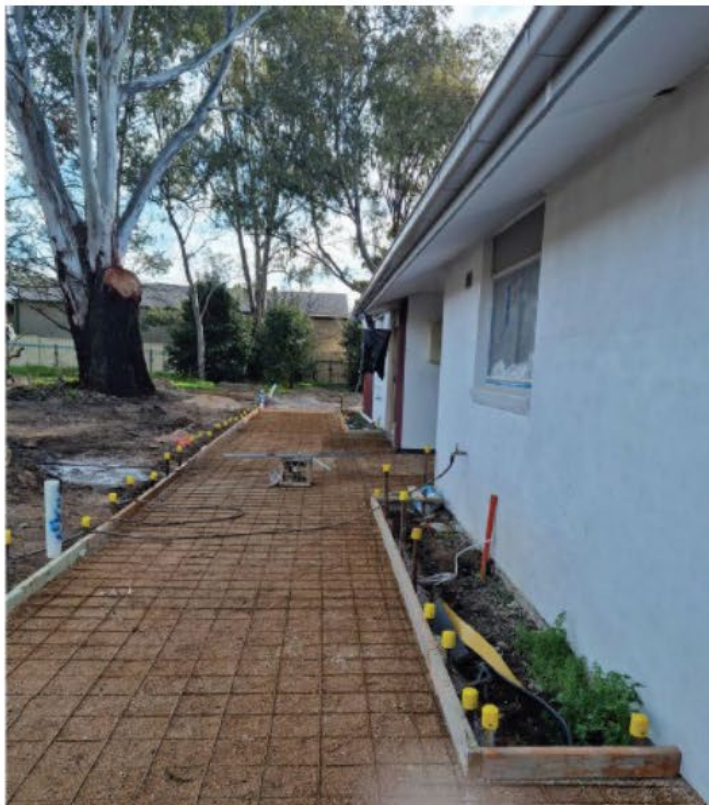

COMMUNITY | MUDGEES ARTS PRECINCT PROJECT PROGRESS REPORT



COMMUNITY | MUDGEES ARTS PRECINCT PROJECT PROGRESS REPORT

